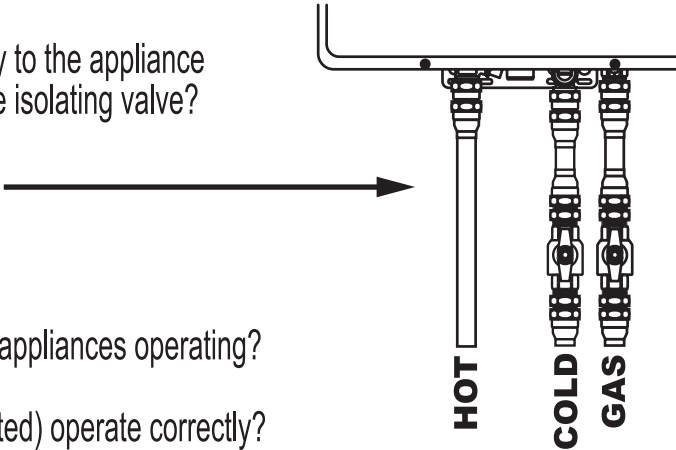



COMMISSIONING CHECK LIST

Attention Installer - have you checked!

- ☐ Gas supply pipe is purged of foreign matter before connection.
- ☐ For Hot and Cold cross connections i.e. Capped breaches / Shower Mixers, taps closed and reversed 'Flick Mixer' connections?
- ☐ That isolating valves are not connected directly to the appliance and there is a means of disconnection after the isolating valve?
- ☐ That plumbing connections are correct? 
- ☐ Have you turned on the power?
- ☐ Is appliance inlet gas pressure correct with all appliances operating?
- ☐ Do the Kitchen and Bathroom Controllers (if fitted) operate correctly?
- ☐ Tempering Valve (if fitted) - Is it an RMC Heat Guard 15/20HP, AVG (Australian Valve Group) TVA-HP series or other equivalent for continuous flow water heater use?
- ☐ Have you checked water temperature at all outlets?
- ☐ Have you cleaned cold water inlet filter?
- ☐ Have you shown the customer how to operate the Temperature Controllers? (If fitted)
- ☐ Have you explained to the Customer the Benefits of Controllers (if not fitted) and that they can be added later?
- ☐ Have you explained to the customer the minimum flow rate required to operate the unit?
- ☐ Have you checked the flue clearances and installation and as per AS5601?

For Internal (FFU) models only

- ☐ Have you used only Rinnai FF flueing components?
- ☐ If flue length exceeds 1.5m, dip-switch 1 of SW1 is to be switched to the 'OFF' position as shown.
- ☐ If flue length exceeds 2m, connect a condensate drain pipe in accordance with the FF flueing instructions.



For ENVIROSMART models.

- ☐ Have you connected a condensate drain pipe in accordance with the installation Instructions.

PLEASE NOTE:

That warranty may be voided and a service charge may be incurred as a result of Rinnai staff attending to a problem related to installation.
